



GREY BANNER ALERT



SHW Serious Incident (SI) – Final Notice

Date of Incident:	27/04/2023	Time of Incident:	2.39pm
Region / Directorate:	RMO – MWG	Main Roads or Contractor:	Contractor
EQSafe Event Type:	Procedural Breach	EQSafe Incident Number:	31000
Actual Consequence:	Insignificant	Potential Consequence:	Catastrophic

Incident Short Description:	Asphalt Workers on Foot within 1.2m of Live Traffic
------------------------------------	---


Executive Summary:

On Thursday 27/04/2023 at approximately 2.40pm Main Roads representatives noticed that, as asphalt works were proceeding, the exclusion zone between the workers on foot and the live traffic lane had decreased to less than the required 1.2m.

The Main Roads Representative advised The Principal Contractor of the Critical Control Breach, following which the works activity was ceased for reassessment.


A compliance review of the TGS was undertaken, the Traffic Control Team stopped traffic in both directions and re-positioned the delineators to allow a minimum exclusion of 1.2m from live traffic.

Incident Photos:

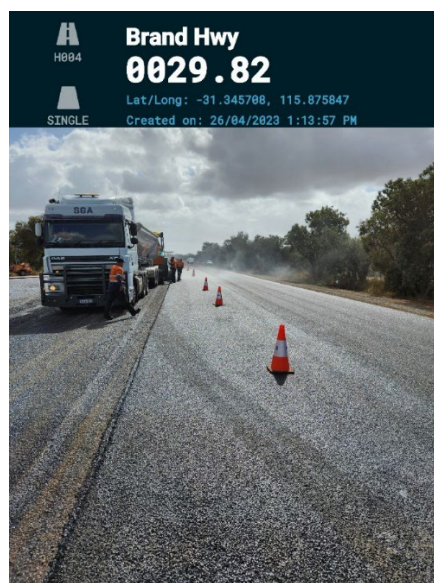

Asphalt Workers working within 1.2m of Live Traffic

Incident Photos:

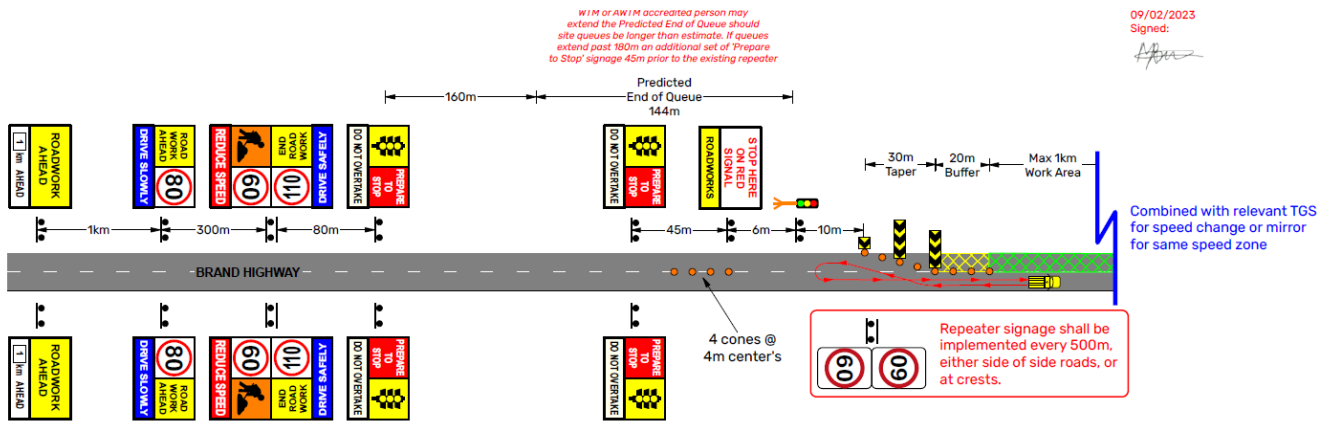

Traffic management implemented for single lane operation with workers on foot greater than 1.2m from trafficable lane

Contributing Factors:

- The Principal Contractor did not complete verification processes to ensure traffic management treatments were correctly implemented for the works.
- Traffic management personnel were not aware of the requirement to reduce the site to 40km or to ensure delineation was adequate to allow minimum of 1.2m from live traffic if running at 60km.
- Asphaltting team were unaware of the requirement to remain at least 1.2m from live traffic with the current traffic management set-up.
- Exclusion zone requirements were not identified or communicated prior to the commencement of works.

Corrective Actions:

- Develop and introduce a Civil and Infrastructure weekly HSEQ Schedule Compliance Dashboard for all MRWA and Resource Based Projects. The schedule is to include Critical Control Verification and Establishment of New Work Locations with a KPI of 100% compliance.
- Ensure all project personnel understand the required exclusion zone distances for specific speed reductions. This can be included in the induction, and prestart communications.
- Supervisor to follow verification processes for ensuring compliance to TMP/TGS.
- Prestart communications to include all workgroups and cover operational requirements for that work.

Additional Issues/Learnings:

An option was available within the Project TMP to reduce site speed to 40km/hr but not considered. The Traffic Team Leader did not risk assess the site to determine if a 40km speed reduction was required.



Critical Risk:

This serious potential incident aligns with the Main Roads Critical Risk Profile relating to **Interaction with Live Traffic.**

Distribution of Notice:

Main Roads Personnel and Contracting Organisations
