



RED BANNER ALERT



SHW Serious Incident (SI) – Preliminary Notice


Date of Incident:	27/04/2023	Time of Incident:	14:39
Directorate / Region:	RMO – MW/G	Main Roads or Contractor:	Contractor
EQSafe Event Type:	Procedural Breach	EQSafe Incident Number:	31000
Actual Consequence:	Insignificant	Potential Consequence:	Catastrophic

Incident Short Description:	Asphalt Workers on Foot within 1.2m of Live Traffic
------------------------------------	---

What Happened:

On Thursday 27/04/2023 at approximately 14:40, Main Roads representatives noticed that as asphalt works were proceeding, the buffer zone between the workers on foot and the live traffic lane had decreased to less than the required 1.2m.

Workers were directed to stop until cones delineating the worksite could be moved to provide the required buffer zone between the workers and live traffic lane.

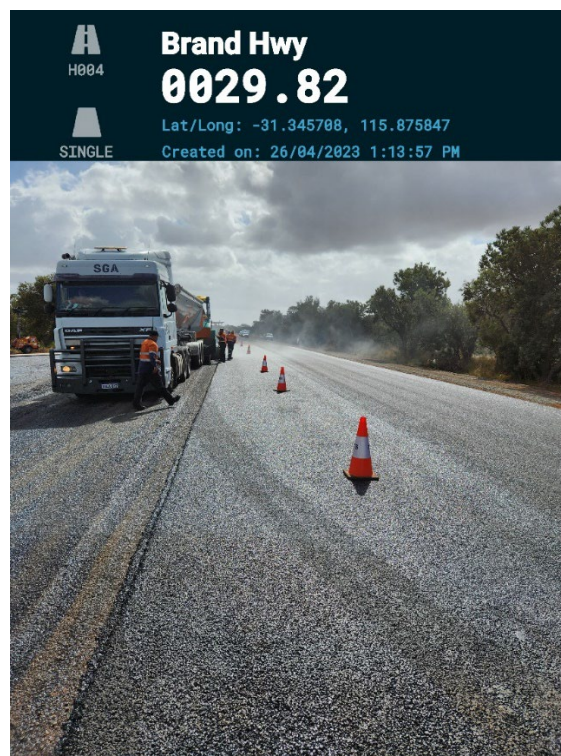

Asphalt Workers working within 1.2m of Live Traffic

A formal ICAM investigation has commenced. Once completed, the lessons learnt will be communicated/shared through a final Grey Banner Alert as soon as practicable.



This serious potential incident aligns with the Main Roads Critical Risk profile relating to **Interaction with Live Traffic**.

Immediate Actions:

Please note that these are generic actions for all to consider in relation to this critical risk (and is not reflective of this specific incident):

- *Ensure that work methodologies clearly communicate Traffic Management requirements for specific works.*
- *Ensure Traffic Controllers are briefed in what is actually required for the specific works - Discuss Critical Risks and the corresponding Critical Controls at Pre-start Meetings.*
- *Use tools such as Critical Risk Observation Checklists to verify that Critical Controls are in place and are effective at the start of a task and as required thereafter.*

Distribution of Notice:	Main Roads Personnel and Contracting Organisations
--------------------------------	--
