

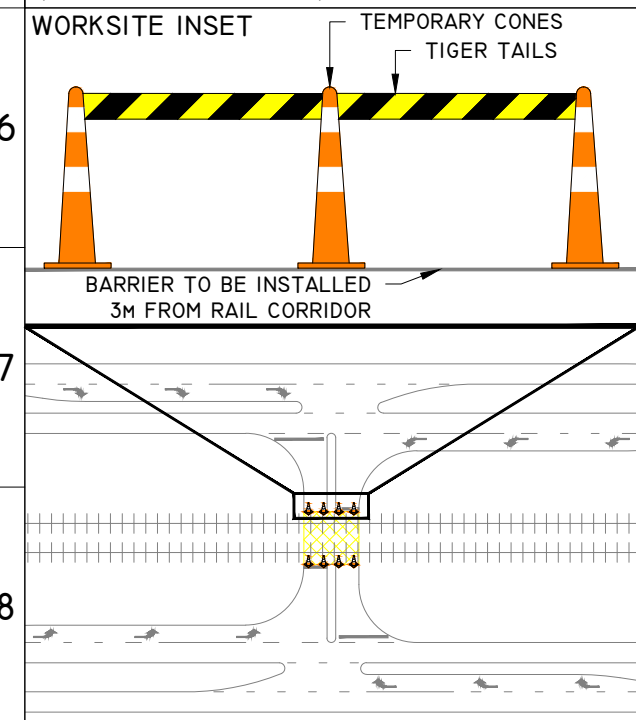


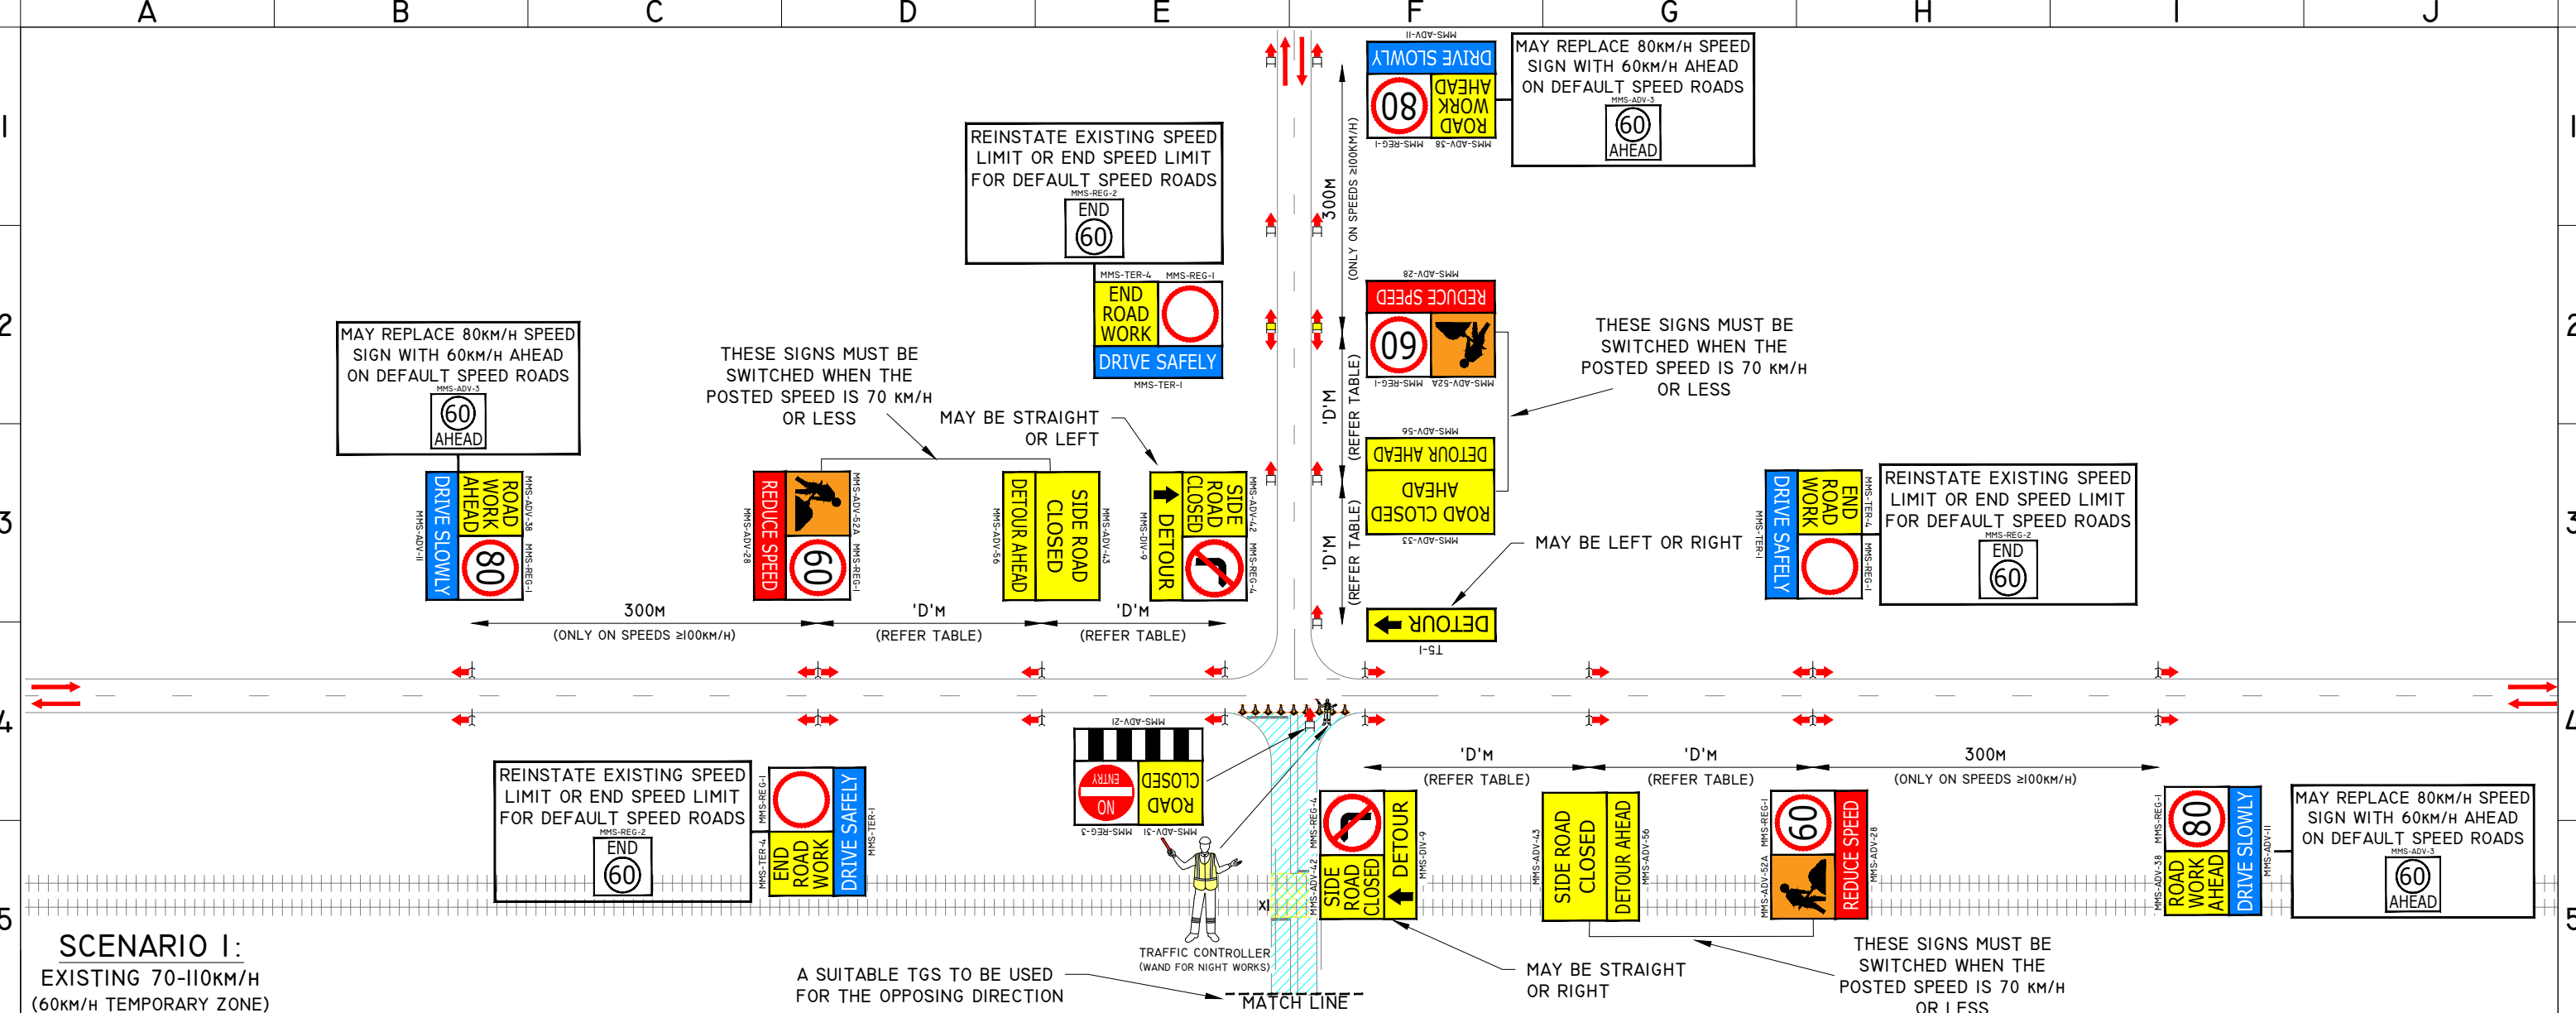

TABLES	
SIGN SPACING	
AGTTM PART 3 - TABLE 2.2	
SPEED LIMIT (KM/H)	DISTANCE ('D')
55 OR LESS	15
56 TO 65	45
GREATER THAN 65	EQUAL TO SPEED OF TRAFFIC IN KM/H

NOTES	
RECOMMENDED CONE SPACING AGTTM PART 3 - TABLE 5.3 ALL PURPOSES: (60 - 70KM/H): 12M PROTECTING FRESHLY PAINTED LINES: (≤ 70KM/H): 24M RECOMMENDED LANE WIDTHS MAIN ROADS WA CoP SECTION 6.7 - TABLE 9 RECOMMENDED LANE WIDTHS: ≤ 60KM/H: 3.2M MINIMUM LANE WIDTHS: ≤ 60KM/H: 3.0M	
 XI ACCREDITED FLAG PERSON TO BE POSITIONED ON SITE TO WARN OF INCOMING TRAINS WHERE WORKS ARE LESS THAN 3M TO RAIL LINE. WORKERS TO CLEAR WORKSITE AND TRAIN PATH AS REQUIRED	

- TOLERANCES**
POSITION OF SIGNS:
MINIMUM 10% LESS THAN THE DISTANCE OR LENGTHS GIVEN.
MAXIMUM 25% MORE THAN THE DISTANCES OR LENGTHS GIVEN.
SPACING OF DELINEATING DEVICES:
MAXIMUM 10% MORE THAN THE SPACING GIVEN.
NO MINIMUM.
AGTTM PART 6 SECTION 6.8.
- DOCUMENTATION**
ON-SITE VARIATIONS MUST BE APPROVED BY THE TRAFFIC MANAGEMENT SUPERVISOR, THAN AN ON-SITE VARIATION MADE AND CHANGES RECORDED IN THE DAILY DAIRY. FOR MORE INFORMATION REFER TO SECTION 9.3 OF THE TMP.
- A RISK ASSESSMENT MUST BE CARRIED OUT TO DETERMINE THE REQUIREMENTS OF AFTERCARE.
 - ALL SIGN LOCATIONS ARE TO BE CHECKED ON SITE PRIOR TO SETOUT AND POSITIONS ADJUSTED AS PER THE 'TOLERANCES'.
 - ALL CONTRADICTORY SIGNS WITHIN THE TM SETUP TO BE COVERED BY SUITABLY OPAQUE MATERIAL.
 - FOR BOX EDGED SIGN ALTERNATIVES, CONSULT AWTM PRIOR TO IMPLEMENTATION.
 - WORKERS TO REMAIN 10M CLEAR OF RAILWAY TRACKS AT ALL TIMES.
 - ACCREDITED FLAG PERSON TO MONITOR AND WARN OF INCOMING TRAINS OVER TWO-WAY RADIO. TCS WILL HOLD ALL TRAFFIC TO ALLOW TRAIN TO PASS.
 - REFER TO SECTION 4.1.8 OF THE TMP FOR THE MANDATORY USE OF SPEED FEEDBACK SIGNAGE
- PEDESTRIAN MANAGEMENT**
- 'PEDESTRIAN WATCH YOUR STEP' SIGN TO BE INSTALLED ON EACH APPROACH WHERE WORKS MAY ENCR OACH ONTO OR ADJACENT TO EXISTING FOOTPATH FACILITIES.
 - TM PERSONNEL TO MONITOR AND ESCORT PEDESTRIANS THROUGH THE WORK AREA AS REQUIRED.
 - PEDESTRIANS MAY BE HELD ON EITHER END OF THE WORKSITE UNTIL IT IS SAFE TO PASS AS REQUIRED.
