



RED BANNER ALERT



SHW Serious Incident (SI) – Preliminary Notice

Date of Incident:	25/11/2022	Time of Incident:	11:00am
Directorate / Region:	RMO – Goldfields Esperance Regions	Main Roads or Contractor:	Contractor
EQSafe Event Type:	SHW Procedure Breach	EQSafe Incident Number:	29210
Actual Consequence:	Insignificant	Potential Consequence:	Major

Incident Short Description:	Traffic Controller positioning themselves close to the live lane
------------------------------------	--

What Happened:

At approximately 11:00am on 25/11/2020, a Main Roads worker observed a TC (Traffic Controller) using hand signals to re-direct traffic back into the natural lane thereby placing themselves closer to the live traffic lane.

During a discussion with the TC, the Main Roads worker was advised that earlier that morning a vehicle had not returned to the correct lane (eastbound) on the departure end of the lane closure when there was no traffic stopped at the traffic lights, and instead proceeded in the westbound lane past the stop point before returning to the correct eastbound lane.

The Main Roads worker highlighted the dangers to TC regarding getting too close to the traffic lane. The Traffic Management Representative brought it to the attention of the crew leader and reiterated that TCs are not to step into the lane and are to keep out of the "line of fire". Traffic Management Representative explored options to prevent traffic not returning to its natural lane and arranged for the event to be discussed at the next prestart meeting.

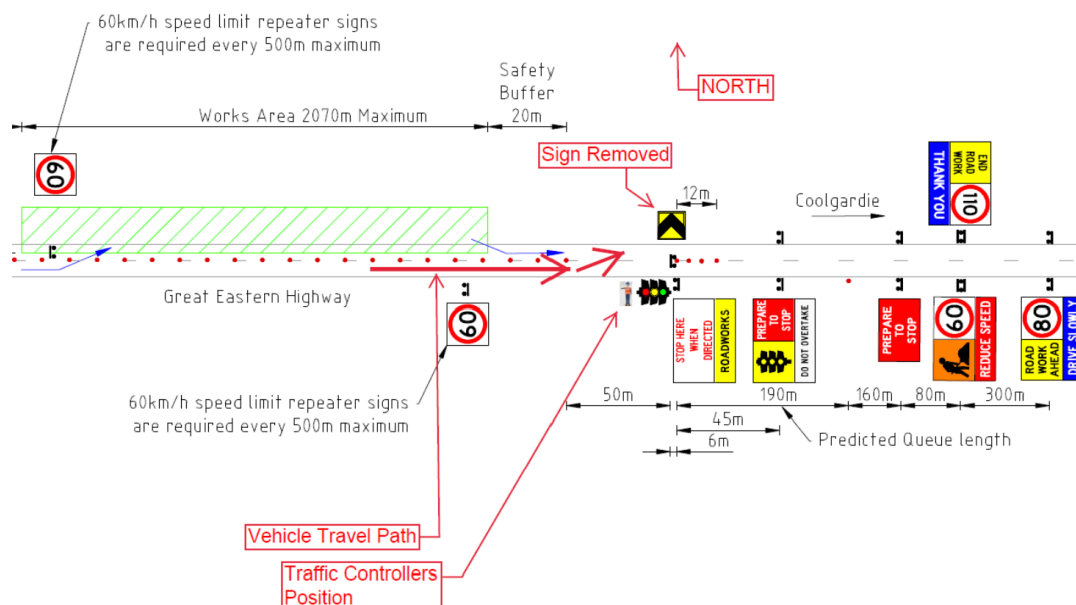


Diagram of the TM setup and incident

A formal ICAM investigation has commenced. Once completed, the lessons learnt will be communicated/shared through a final Grey Banner Alert as soon as practicable.



This serious potential incident aligns with the Main Roads Critical Risk profile relating to **Interaction with Live Traffic**.

Immediate Actions:

Please note that these are generic actions for all to consider in relation to this critical risk (and is not reflective of this specific incident):

- *Maintain safe working distances from traffic, always have an escape route.*
- *Check that controls identified in the project risk register for working near live traffic are understood by workers and put in place on site.*
- *Ensure Traffic Management is reviewed regularly to ensure compliance to the Traffic Management Plan TMP along Traffic Guidance Scheme TGS.*

Distribution of Notice:

Main Roads Personnel and Contracting Organisations
