



GREY BANNER ALERT



SHW Serious Incident (SI) – Final Notice

Date of Incident:	26 April 2022	Time of Incident:	1330
Region / Directorate:	GSR	Main Roads or Contractor:	Contractor
EQSafe Event Type:	Injury/Illness	EQSafe Incident Number:	26755
Actual Consequence:	Moderate	Potential Consequence:	Moderate


Incident Short Description:	8 tonne double drum roller slides down batter and overturns.
------------------------------------	--

Executive Summary:
At approximately 13:30 hrs on 26 April 2022, a contractor team were using an 8-tonne vibrating twin steel drum roller to compact the prepared shoulder material. The roller was working in tandem with a grader; the operator was rolling in a forward direction with the outer edge of the drum close to the edge of the shoulder material. The roller operator felt the roller machine become unstable and stopped the machine. The roller operator notified the grader operator that the roller was unstable and suggested using a wheeled excavator – which was also available on site – to help move the roller back to stable ground. The grader operator was reported to have advised they would be able to move the roller and there would be no requirement to use the excavator. The grader operator attempted to move the roller back to stable ground; the roller slipped off the edge batter and tipped onto its side. The operator was wearing their seat belt and was able to leave the roller safely. The operator was taken to hospital for assessment; it was identified they had sustained a shoulder injury which required surgical intervention. The roller received significant damage and required a crane to recover the machine.

Incident Photos:



View 1: Overturned Drum Roller

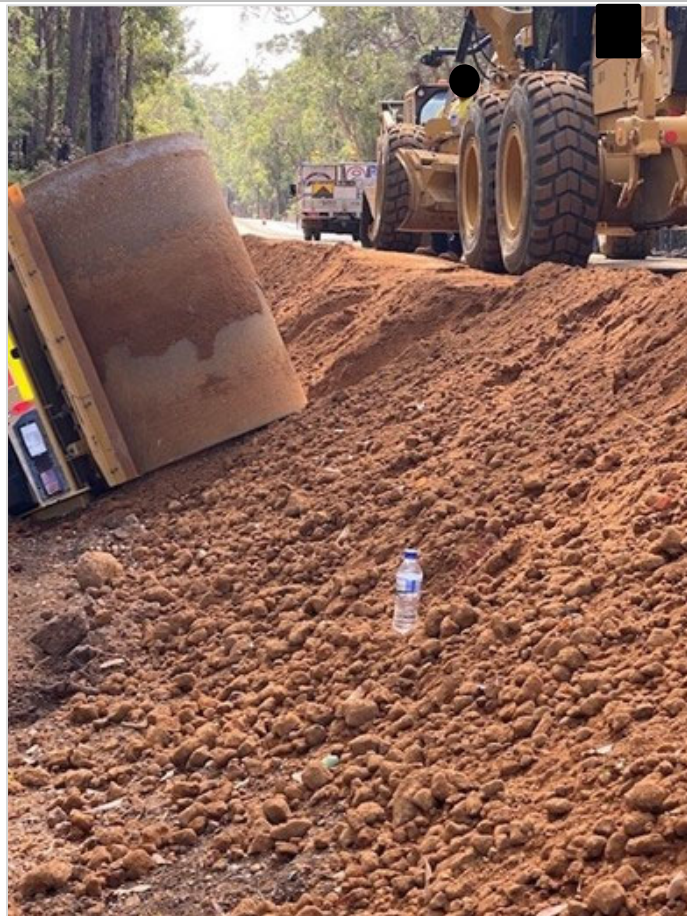

View 2: Overturned Drum Roller



View 3: Overturned Drum Roller

Contributing Factors:

- The Site recovery procedure was not followed. Passively tolerated violation of recovery procedure by the subcontractor.
- The injured person (IP) did not adequately assess risk.
- The IP's perception of hazards associated with recovering the drum roller was different to that of the roller operator.
- Soft shoulder and steep incline.
- Noted in pre-start that rain was expected at lunch time.

Corrective Actions:

- Review of the Subcontractor risk management process with respect to the recovery of machinery.
- Issue a Contractor Company Stop Work for Safety Reset.



Critical Risk:

This serious potential incident aligns with the Main Roads Critical Risk Profile relating to '**Mobile Plant.**'

Distribution of Notice:

Main Roads Personnel and Contracting Organisations
